

DEC 16

Work Order ID 153690

153690

Page 1

Thursday, November 24, 2016 10:41:27 AM

Item ID: D3053-042 Accept *N900040100* Setup Start *NS1*
Revision ID: Stop *NS2*
Item Name: 212 Basket Base Assembly
Start Date: 12/5/2016 Start Qty: 1.00 *1* Cust Item ID:
Required Date: 12/13/2016 Req'd Qty: 1.00 *1* Customer:
Reference:

Approvals: Process Plan:  Date: 16-11-24 Tooling: Date: Run Start *NR1*
QC: Date: SPC (Y/N): Date: Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D3053	C

100	Large Fab	0.00
-----	-----------	------

100

Large Fab

Large Fab

Memo

0.44

1-Cut 5 D2235-3 FROM D3166-1 using DT8365

2-Cut Ribs from 3/4" x 3/4" x 0.065 wall 304/316 SS tubing as per dwg.

3-Remove all markings from material

4-Drill holes in D3053-3 as per dwg D3053

5-Drill holes in three D2235-3 ribs as per dwg D3053 using DT8995

6- Cut mesh as per dwg

1 NOV 28 2016 DAS 24 9-89

110

110

Large Fab

Large Fab

Weld per dwg A/R S.S. rod Batch: 3134107 0.00

Large Fab

Memo

0.00

1 -Weld as per Dwg D3053 using Welding Table and corner Jig Deburr as required

1x CC 16-12-5

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Set-up ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : _____					

Work Order ID 153690***153690***

Page 2

Thursday, November 24, 2016 10:41:27 AM

Item ID: D3053-042

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: 212 Basket Base Assembly

Start Date: 12/5/2016 Start Qty: 1.00

1

Cust Item ID:

Required Date: 12/13/2016 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Start

NR1

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

120

QC9- Inspect visual per QSI004- Fusion Welds

0.00

120

QC

Memo

0.00

Quality Control

D 16-12-06

DAS
9
9-89

130

QC6- Inspect dimensions to drawing

0.00

130

QC

Memo

0.00

Quality Control

QCSD
PTO

D 16-12-06

DAS
9
9-89

140

Pressure Wash per QSI005 4.3

0.00

140

HandFinish

Memo

0.00

Hand Finishing

1 16-12-07

BEB

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only



Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		DAS 9 161206 Completed By DAS 10 9-89	
change to QCS					
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	

Root Cause			FAULT CATEGORY		
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐
Past Expiry Date ☐	Manufacturing Process ☐				
Misidentified ☐	Past Due ☐	OTHER : _____			

Work Order ID 153690

Thursday, November 24, 2016 10:41:27 AM

153690

Page 3

Item ID: D3053-042 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: 212 Basket Base Assembly
Start Date: 12/5/2016 Start Qty: 1.00 ***1*** Cust Item ID:
Required Date: 12/13/2016 Req'd Qty: 1.00 ***1*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
150 *150* Powdercoat Powder Coating	White Gloss(Ref:4.3.5.2) per OSI005 4.3-Steel <i>M135418</i> Memo START TIME: <i>1:50</i> OVEN TEMPERATURE: <i>400</i> FINISH TIME: <i>2:20</i>	0.00 0.14				<i>1</i>	<i>0</i>	<i>16/12/07</i>	<i>333</i>
160 *160* QC Quality Control	QC3- Inspect Part Finish Memo	0.00 0.00				<i>16</i>	<i>0</i>	<i>16/12/08</i>	
170 *170* Packaging Packaging	Identify as per dwg & Stock Location: <i>w/c</i> Memo	0.00 0.00			<i>D205-541-041 B153680</i>	<i>10</i>	<i>0</i>	<i>16/12/09</i>	

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____																																																									
Description Work Order Deviation				Disposition																																																													
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____			
Misidentified ☐	Past Due ☐																																																																

Work Order ID 153690***153690***

Page 4

Thursday, November 24, 2016 10:41:27 AM

Item ID: D3053-042 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: 212 Basket Base Assembly
Start Date: 12/5/2016 Start Qty: 1.00 ***1*** Cust Item ID:
Required Date: 12/13/2016 Req'd Qty: 1.00 ***1*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
180	QC21- Final Inspection - Work Order Release	0.00							
180									
QC	Memo	0.02							
Quality Control									

DAS
21
9-89
DEC 1 2 2016

DAS
21
9-89
DEC 1 2 2016

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																													
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____																																																									
Description Work Order Deviation				Disposition																																																													
Root Cause		FAULT CATEGORY																																																															
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____			
Misidentified ☐	Past Due ☐																																																																

Picklist Print

Thursday, November 24, 2016 10:41:34 AM

Page 1

Work Order ID: 153690

153690

Parent Item: D3053-042

D3053-042

Parent Item Name: 212 Basket Base Assembly

Start Date: 12/5/2016

Required Date: 12/13/2016

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP C02.09.04M304EX0.75-16F was M750-16FXS-S/SKJ/RF
IPP Rev:D 08-08-29 revB as per dwg DD verified by:EC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
---------------------------------	------------------------	---------------	-------------	---------------------	------------------	-----------------	--------------------	----------------	-------------	--------------	---------------	----------------	--------

D3166-1		Manufactured	No			100	Each	18.0000	5	5			
D3166-1									**			DAS 24	DEC 05 2016
Basket Hoop												9-89	

Location	Loc Qty	Loc Code
WA004	18	
145815	8	
148678	8	
148679	2	

M304EX0.75-16F		Purchased	No			100	sf	934.7200	48	50.52632			
M304EX0 75-16F									**			CC 16-12-5	
Expanded Metal Flat SS													

Location	Loc Qty	Loc Code
WA004	934.71996	
M134954	11.99996	
M135485	37.72	
M135660	480	
M136012	405	

M304TS0.750W.065		Purchased	No			100	f	739.0000	43.3333	45.614			
M304TS0 750W 065									**			DAS 24	DEC 05 2016
304 SQ Tube .75x.75x.065W												9-89	

Location	Loc Qty	Loc Code
WA004	739	
m133412	339	
m135655	400	

45.62

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :							
Misidentified ☐	Past Due ☐								

Picklist Print

Thursday, November 24, 2016 10:41:34 AM

Page 2

Work Order ID: 153690

153690

Parent Item: D3053-042

D3053-042

Parent Item Name: 212 Basket Base Assembly

Start Date: 12/5/2016

Required Date: 12/13/2016

Start Qty: 1.00

Required Qty: 1.00

D2232-3 Manufactured No

110 Each 24.0000 2 2

D2232-3

Basket Hinge

DAS
24
9-89

DEC 05 2016

Location

Loc Qty

Loc Code

WA004

24

141081

11

143693

1

148935

12

D2327-3 Manufactured No

110 Each 27.0000 2 2

D2327-3

Spacer Bushing

DAS
24
9-89

DEC 05 2016

Location

Loc Qty

Loc Code

WA004

27

136909

4

148585

23

D2581 Manufactured No

110 Each 72.0000 2 2

D2581

Mounting Bracket

DAS
24
9-89

DEC 05 2016

Location

Loc Qty

Loc Code

WA004

72

132771

1

136270

2

139082

2

146089

21

147603

2

148944

26

151990

18

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE







QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step # : _____		QTY Effective : _____			MRB (QSI042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		OTHER : _____					

QTY -041	QTY -042	PART NO	LENGTH A	LENGTH B	DESCRIPTION
X		D3053-041	N/A	N/A	BASKET BASE ASSY
	X	D3053-042	N/A	N/A	BASKET BASE ASSY
2	2	D3053-1		96.00	RIB
2	2	D3053-3		25.50	RIB
6	6	D3053-5	23.73		RIB
3	3	D3053-7	25.31		RIB
3	3	D3053-9	19.48	N/A	RIB
2	2	D2327-3	N/A	N/A	BUSHING
2	2	D2581	N/A	N/A	MOUNTING BRACKET
2	2	D2232-3	N/A	N/A	HINGE PLATE
5	5	D2235-3	N/A	N/A	RIB



D3053-X RIB

NOTES:

- 1) FRAME MATERIAL: AISI 304/316 SS, 3/4 X 3/4 X 0.065 WALL SQUARE TUBING
REF. DART SPEC M304TS0.750W.065
- 2) MESH MATERIAL: 3/4-16F EXPANDED SS
REF DART SPEC M304EX0.75-16F
- 3) FINISH: POWDER COAT ENTIRE ASSEMBLY WHITE (4.3.5.2) PER DART QSI 005 4.3
- 4) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 5) UNITS: INCHES UNLESS OTHERWISE NOTED
- 6) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 7) IDENTIFICATION: NONE
- 8) WEIGHT: N/A
- 9) CUT LENGTH/SHAPE PER DIAGRAM AND PARTS LIST
- 10) WELD PER DART QSI 004

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER


NO. 153690
① 16-11-24


C	ADD -041 VIEWS, ZN B4-2, D4-2, B7-2. RE-ORGANIZE DWG. REF NCR13-2766.	DC	13.12.12
B	FRAME MATERIAL WAS 0.060 WALL. MESH MATERIAL UPDATED. DRAWING MOVED TO "B" FORMAT AND UPDATED TO CURRENT STANDARDS.	AJS	08.07.02
A	NEW ISSUE	RF	01.11.01
REV.	DESCRIPTION	BY	DATE
DESIGN	RF		
DRAWN	DC		
CHECKED	RF		
MFG. APPR.	DD		
APPROVED	HS		
DE APPR.			
DATE	13.12.12		

DART AEROSPACE LTD
HAWKESBURY, ONTARIO, CANADA


DRAWING NO. D3053
TITLE BASKET BASE ASSEMBLY (212)
REV. C
SHEET 1 OF 5
SCALE NTS

COPYRIGHT © 2001 BY DART AEROSPACE LTD
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS
NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT
WRITTEN PERMISSION FROM DART AEROSPACE LTD.

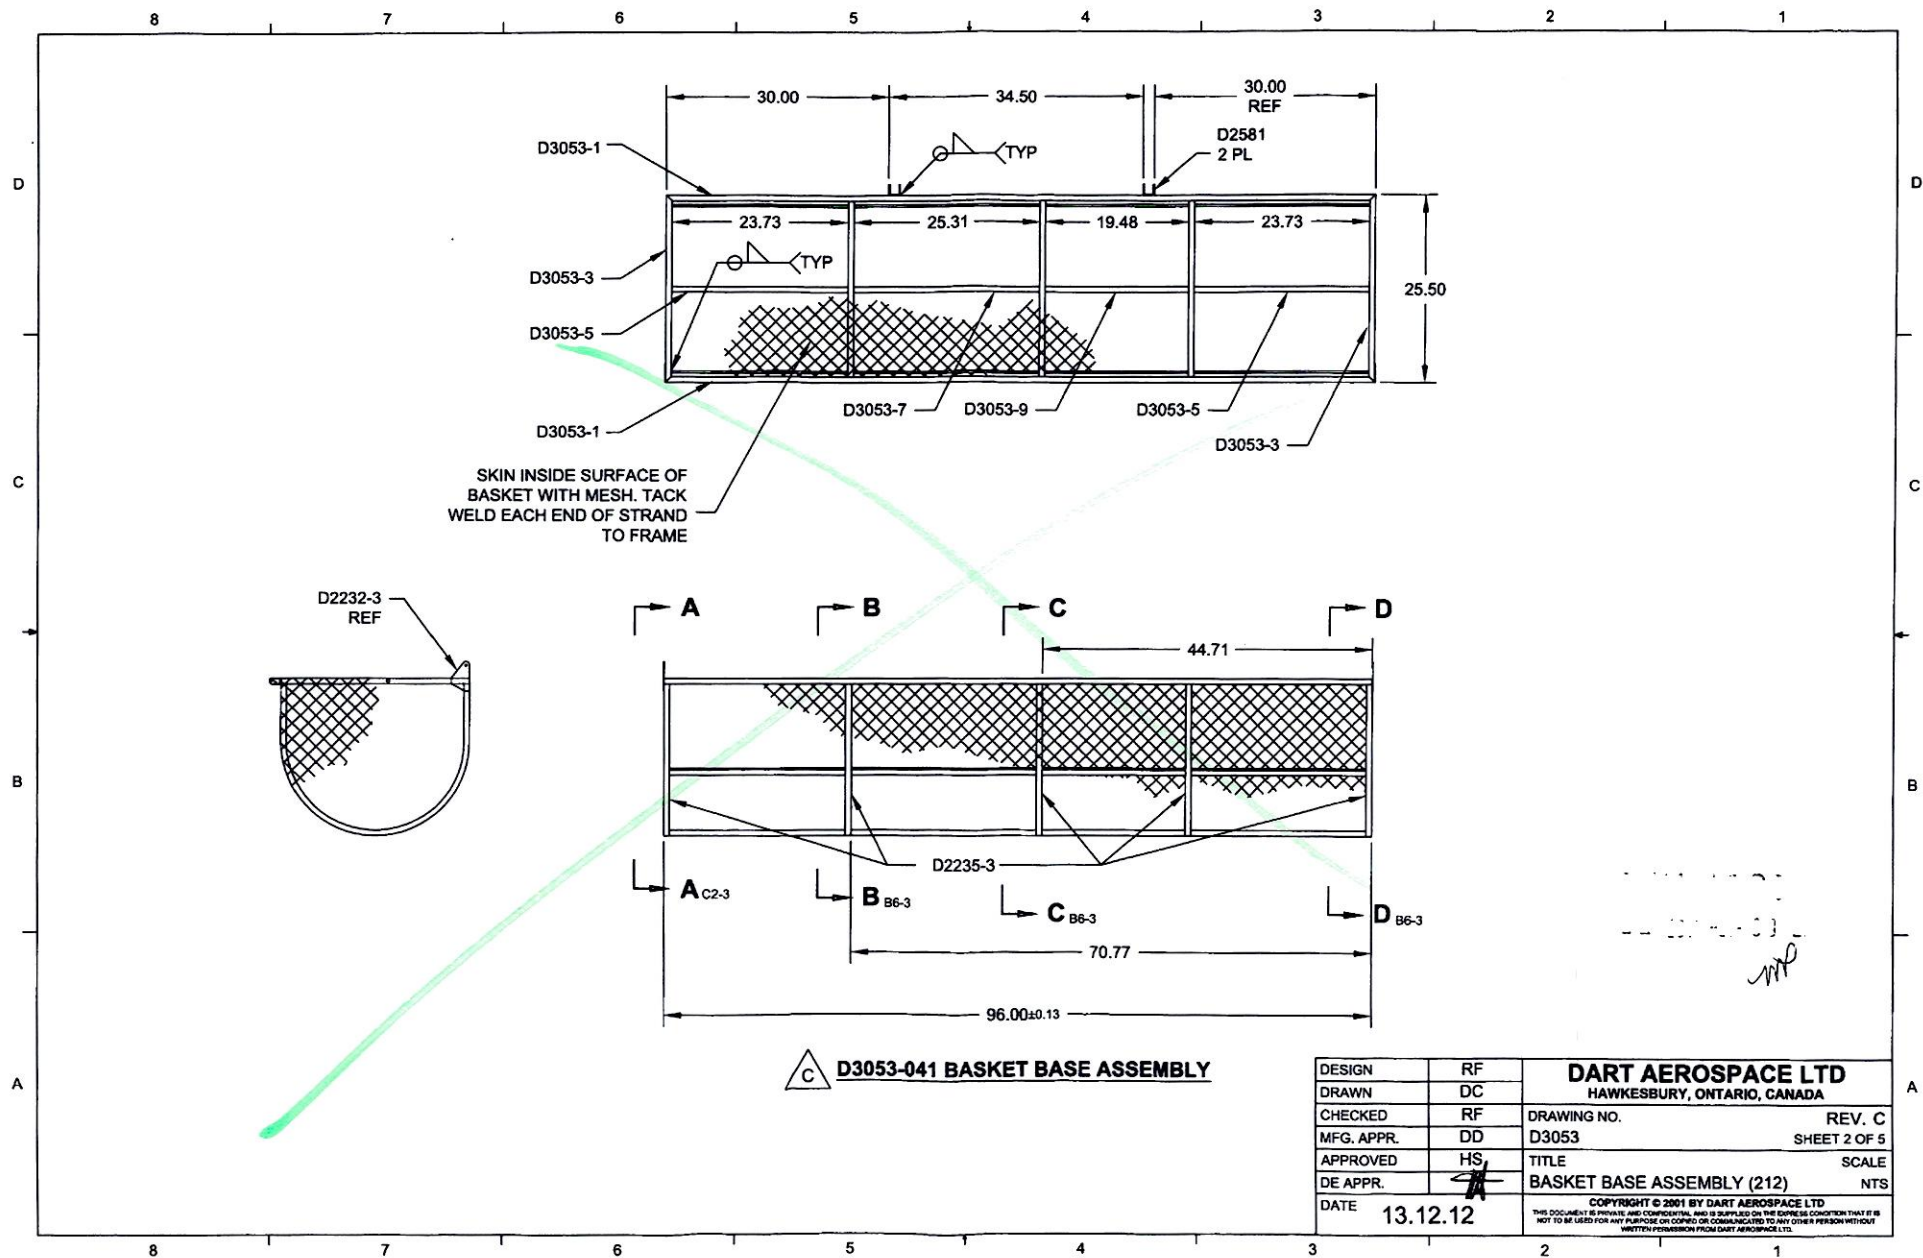


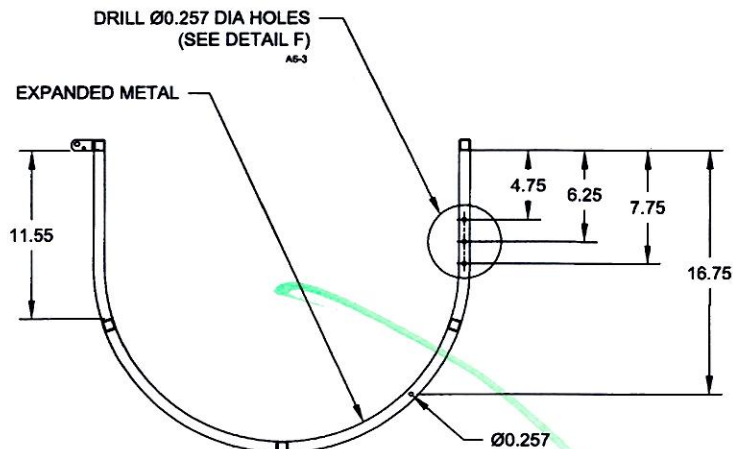


**SECTION B-B_{B5-2}
SECTION C-C_{B4-2}
AND SECTION D-D_{B3-2}**
RIB DETAIL

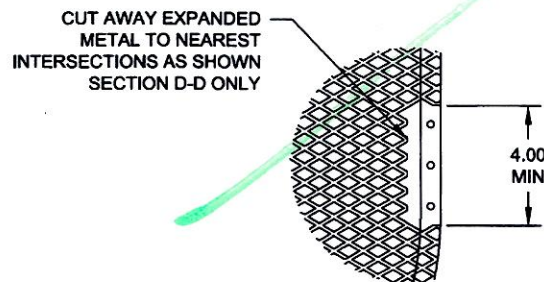

DETAIL F
SCALE NONE
C6-3

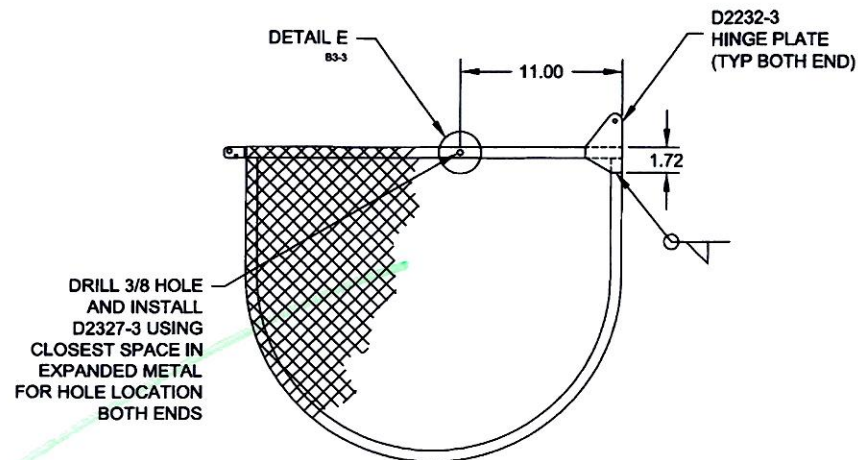


SECTION A-A
SPACER DETAIL
B6-2

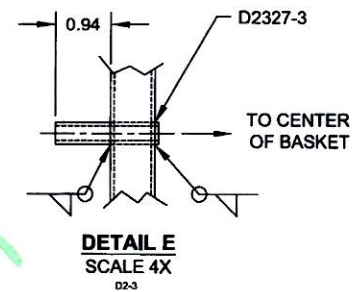


DETAIL E
SCALE 4X
D2-3


DESIGN	RF	DART AEROSPACE LTD	
DRAWN	DC	HAWKESBURY, ONTARIO, CANADA	
CHECKED	RF	DRAWING NO.	REV. C
MFG. APPR.	DD	D3053	SHEET 3 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.		BASKET BASE ASSEMBLY (212)	NTS
DATE	13.12.12	COPYRIGHT © 2001 BY DART AEROSPACE LTD	
		THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

RELEASED
2014-07-03

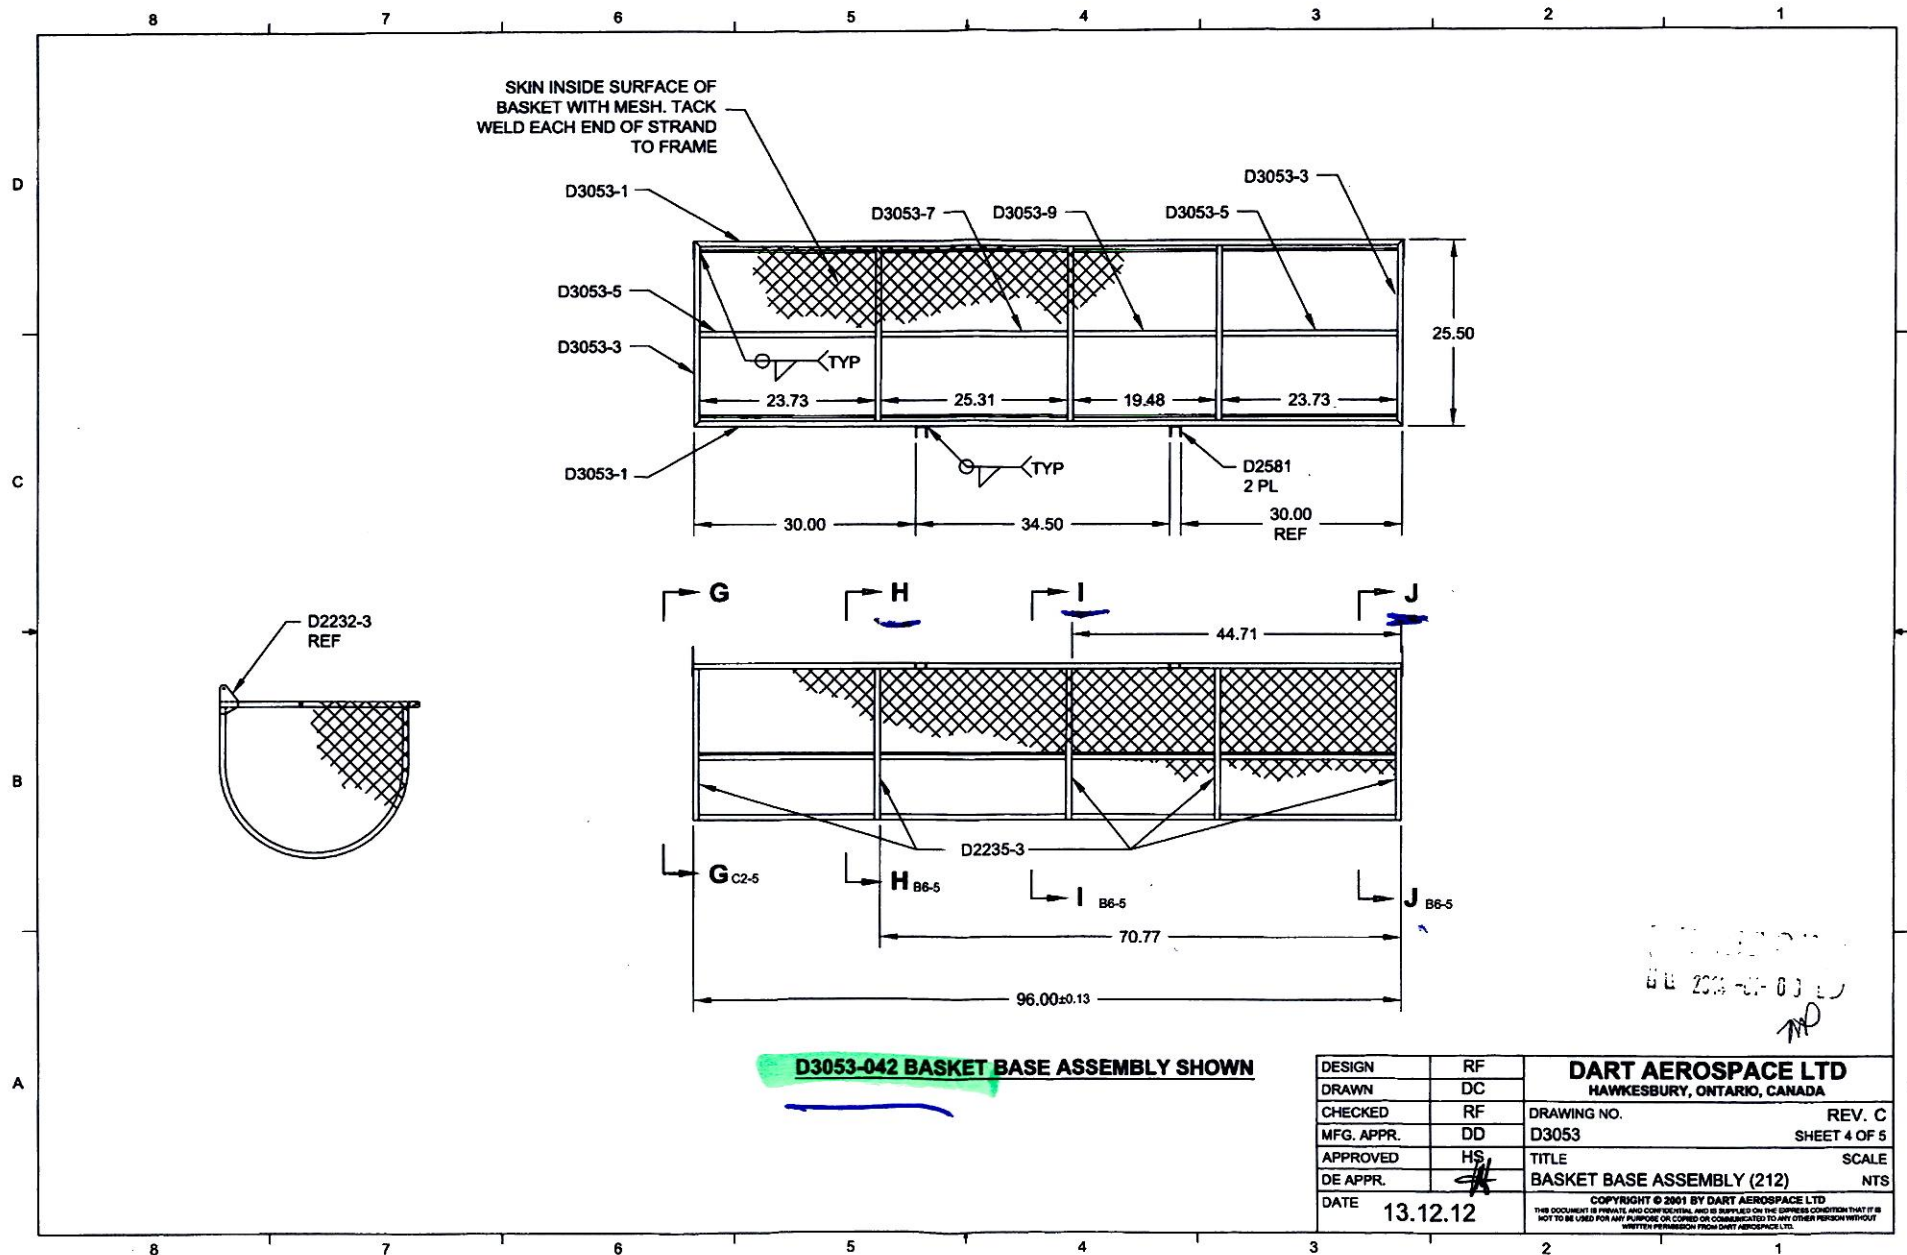


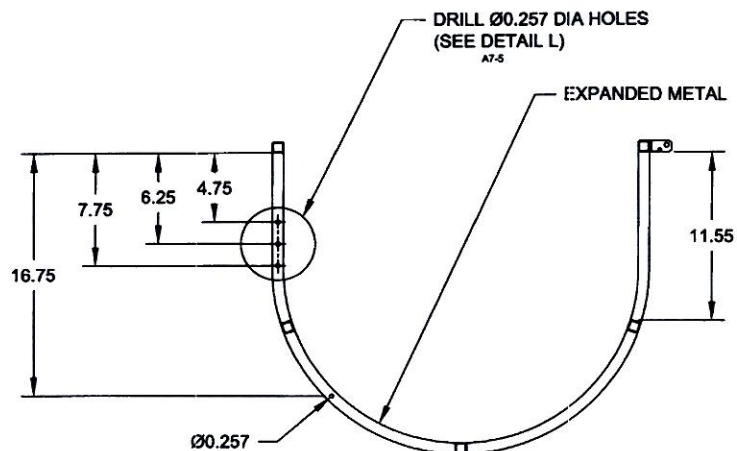


SECTION H-H_{B5-4}
SECTION I-I_{B4-4}
AND SECTION J-J_{B3-4}
RIB DETAIL

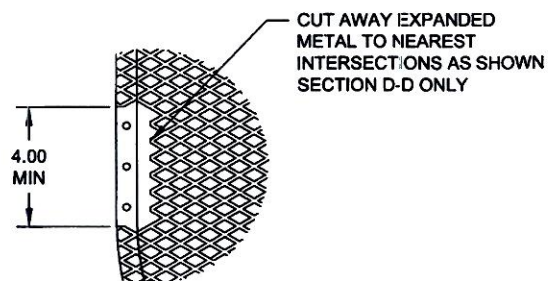

DETAIL L
SCALE NONE
C7-5

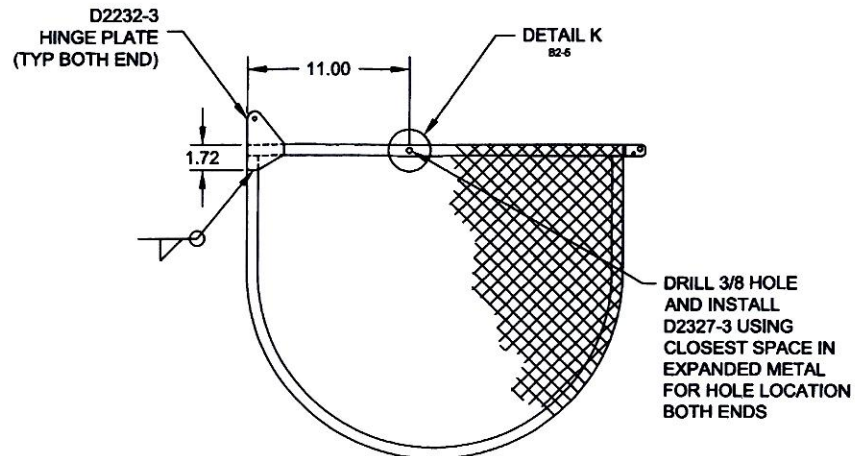

SECTION G-G
SPACER DETAIL
B5-4



DETAIL K
SCALE 4X
D3-5

DESIGN	RF	DART AEROSPACE LTD	
DRAWN	DC	HAWKESBURY, ONTARIO, CANADA	
CHECKED	RF	DRAWING NO.	REV. C
MFG. APPR.	DD	D3053	SHEET 5 OF 5
APPROVED	H9	TITLE	SCALE
DE APPR.		BASKET BASE ASSEMBLY (212)	NTS
DATE	13.12.12	COPYRIGHT © 2001 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
